





City Of Worcester
Department of Public Works & Parks
Water Operations

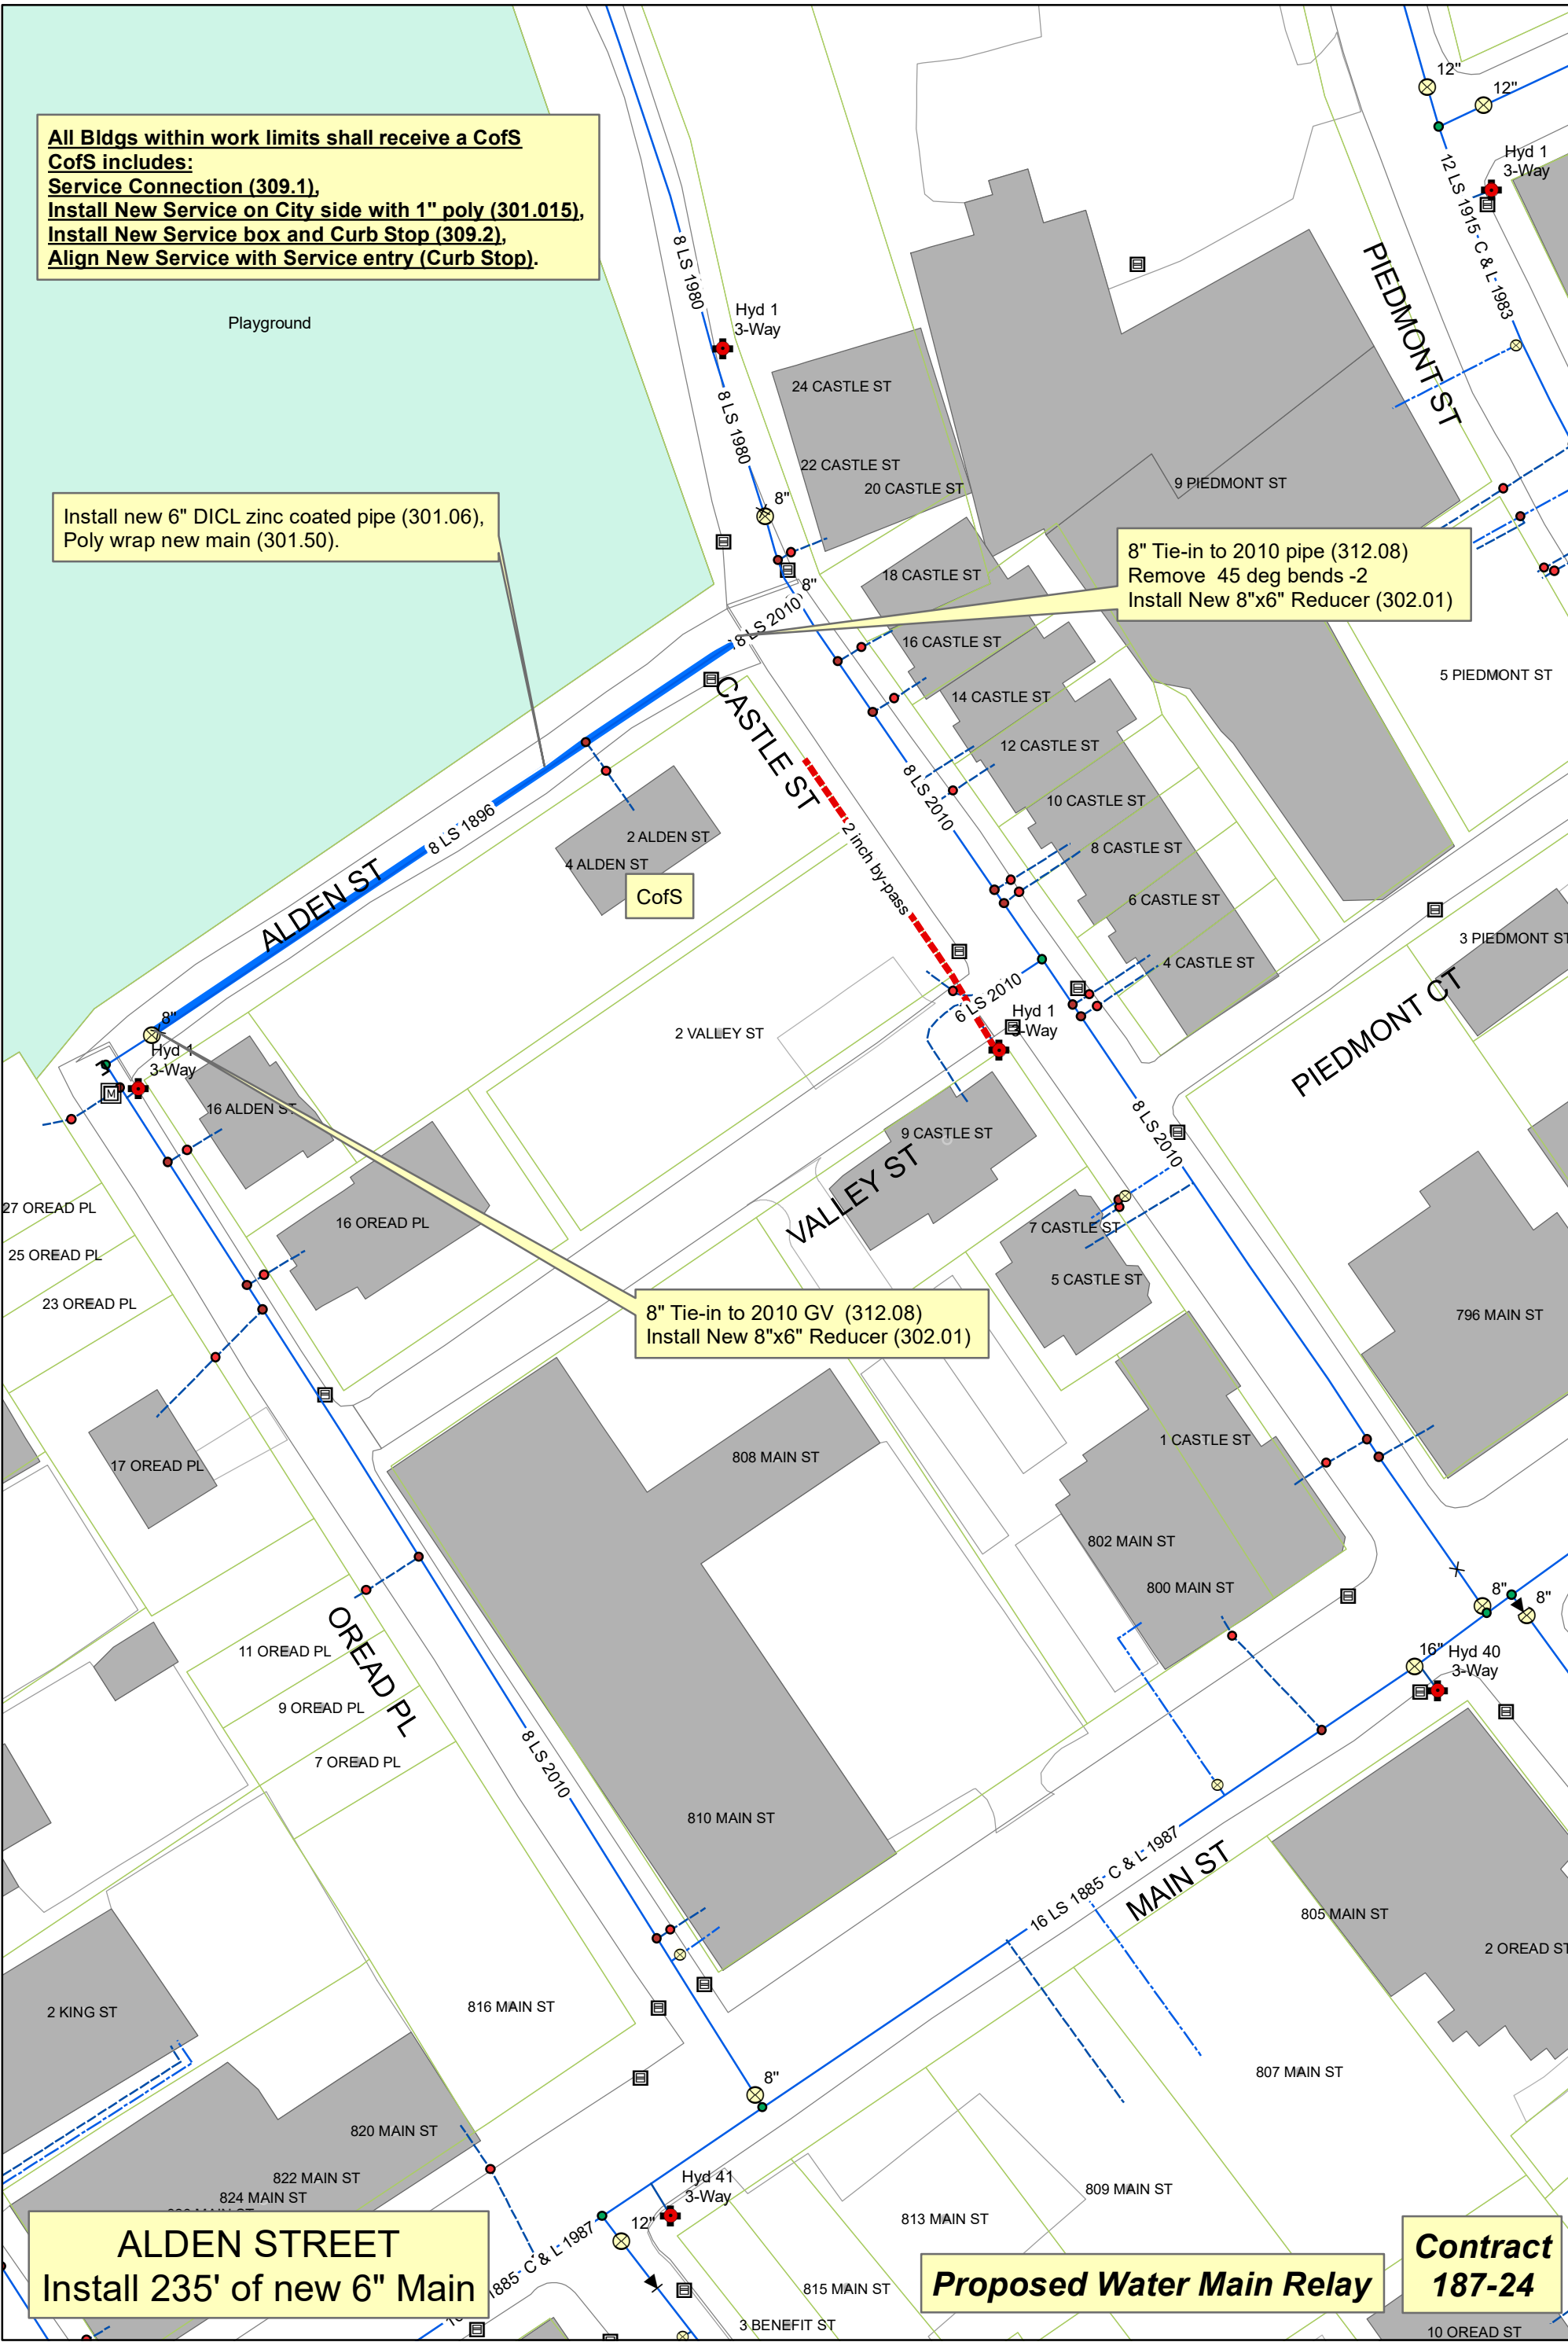





1 inch = 50 feet

0 20 40 80 120 160 Feet




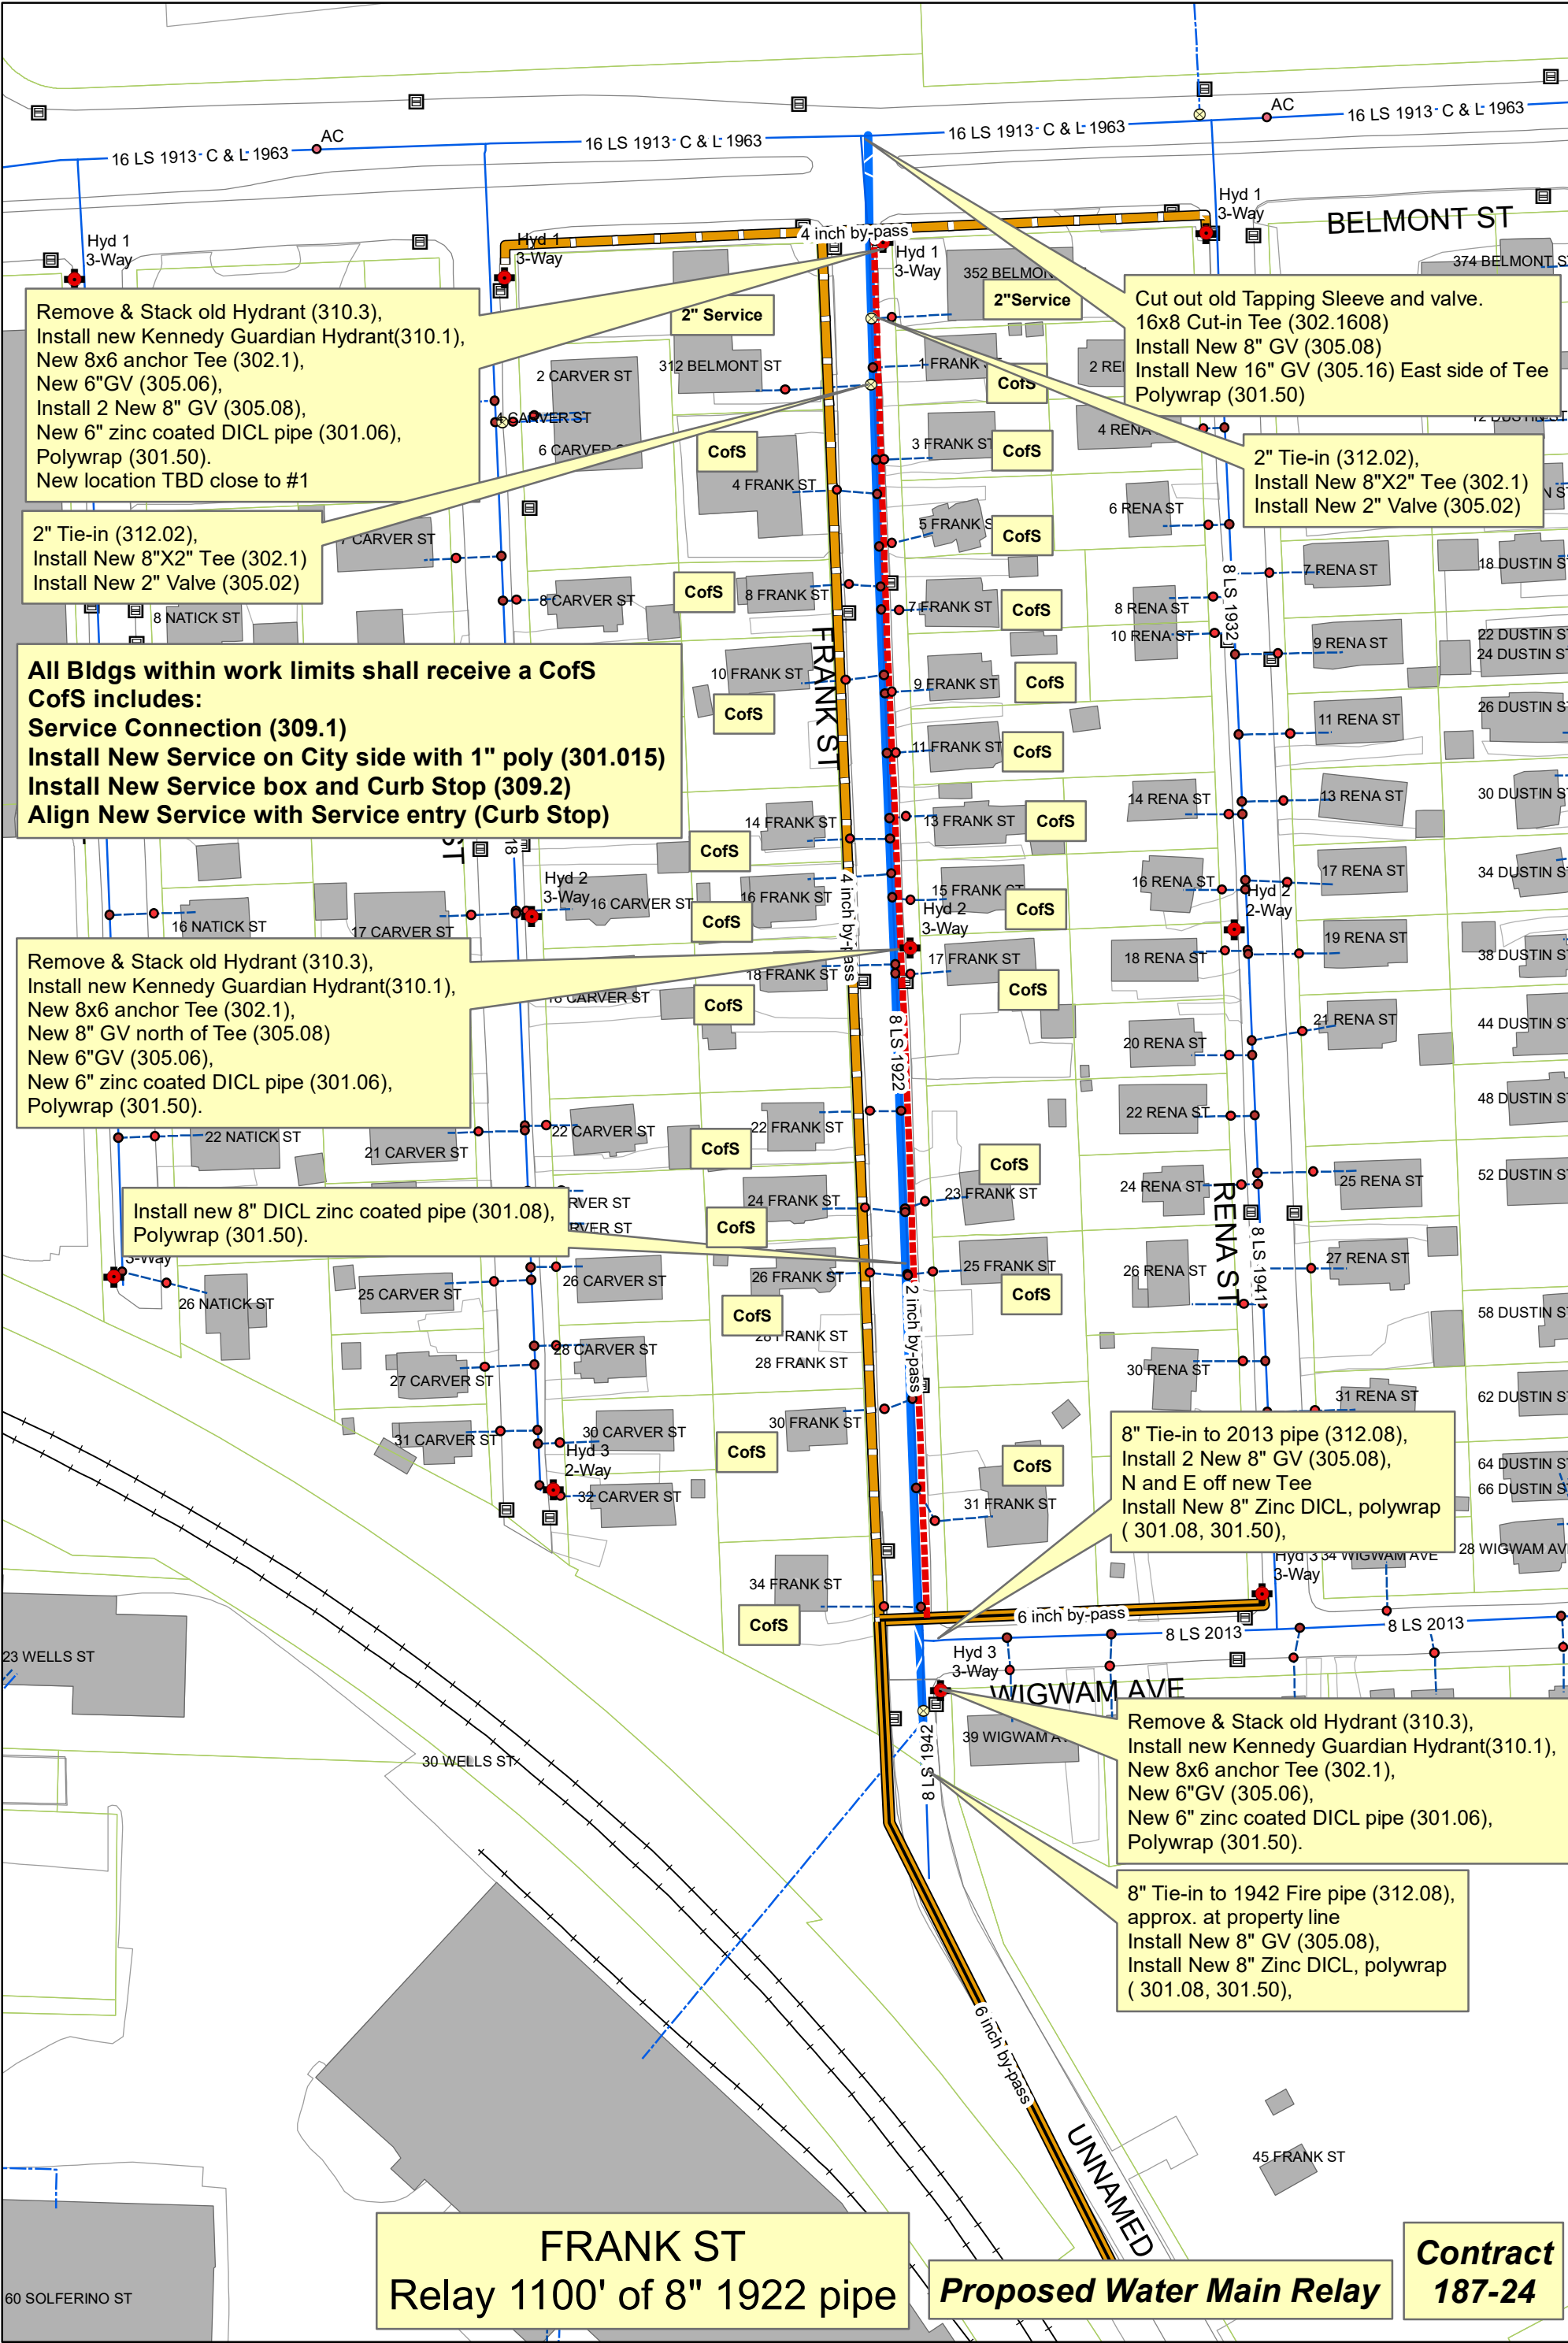

All Bldgs within work limits shall receive a CofS
CofS includes:
Service Connection (309.1)
Install New Service on City side with 1" poly (301.015)
Install New Service box and Curb Stop (309.2)
Align New Service with Service entry (Curb Stop)

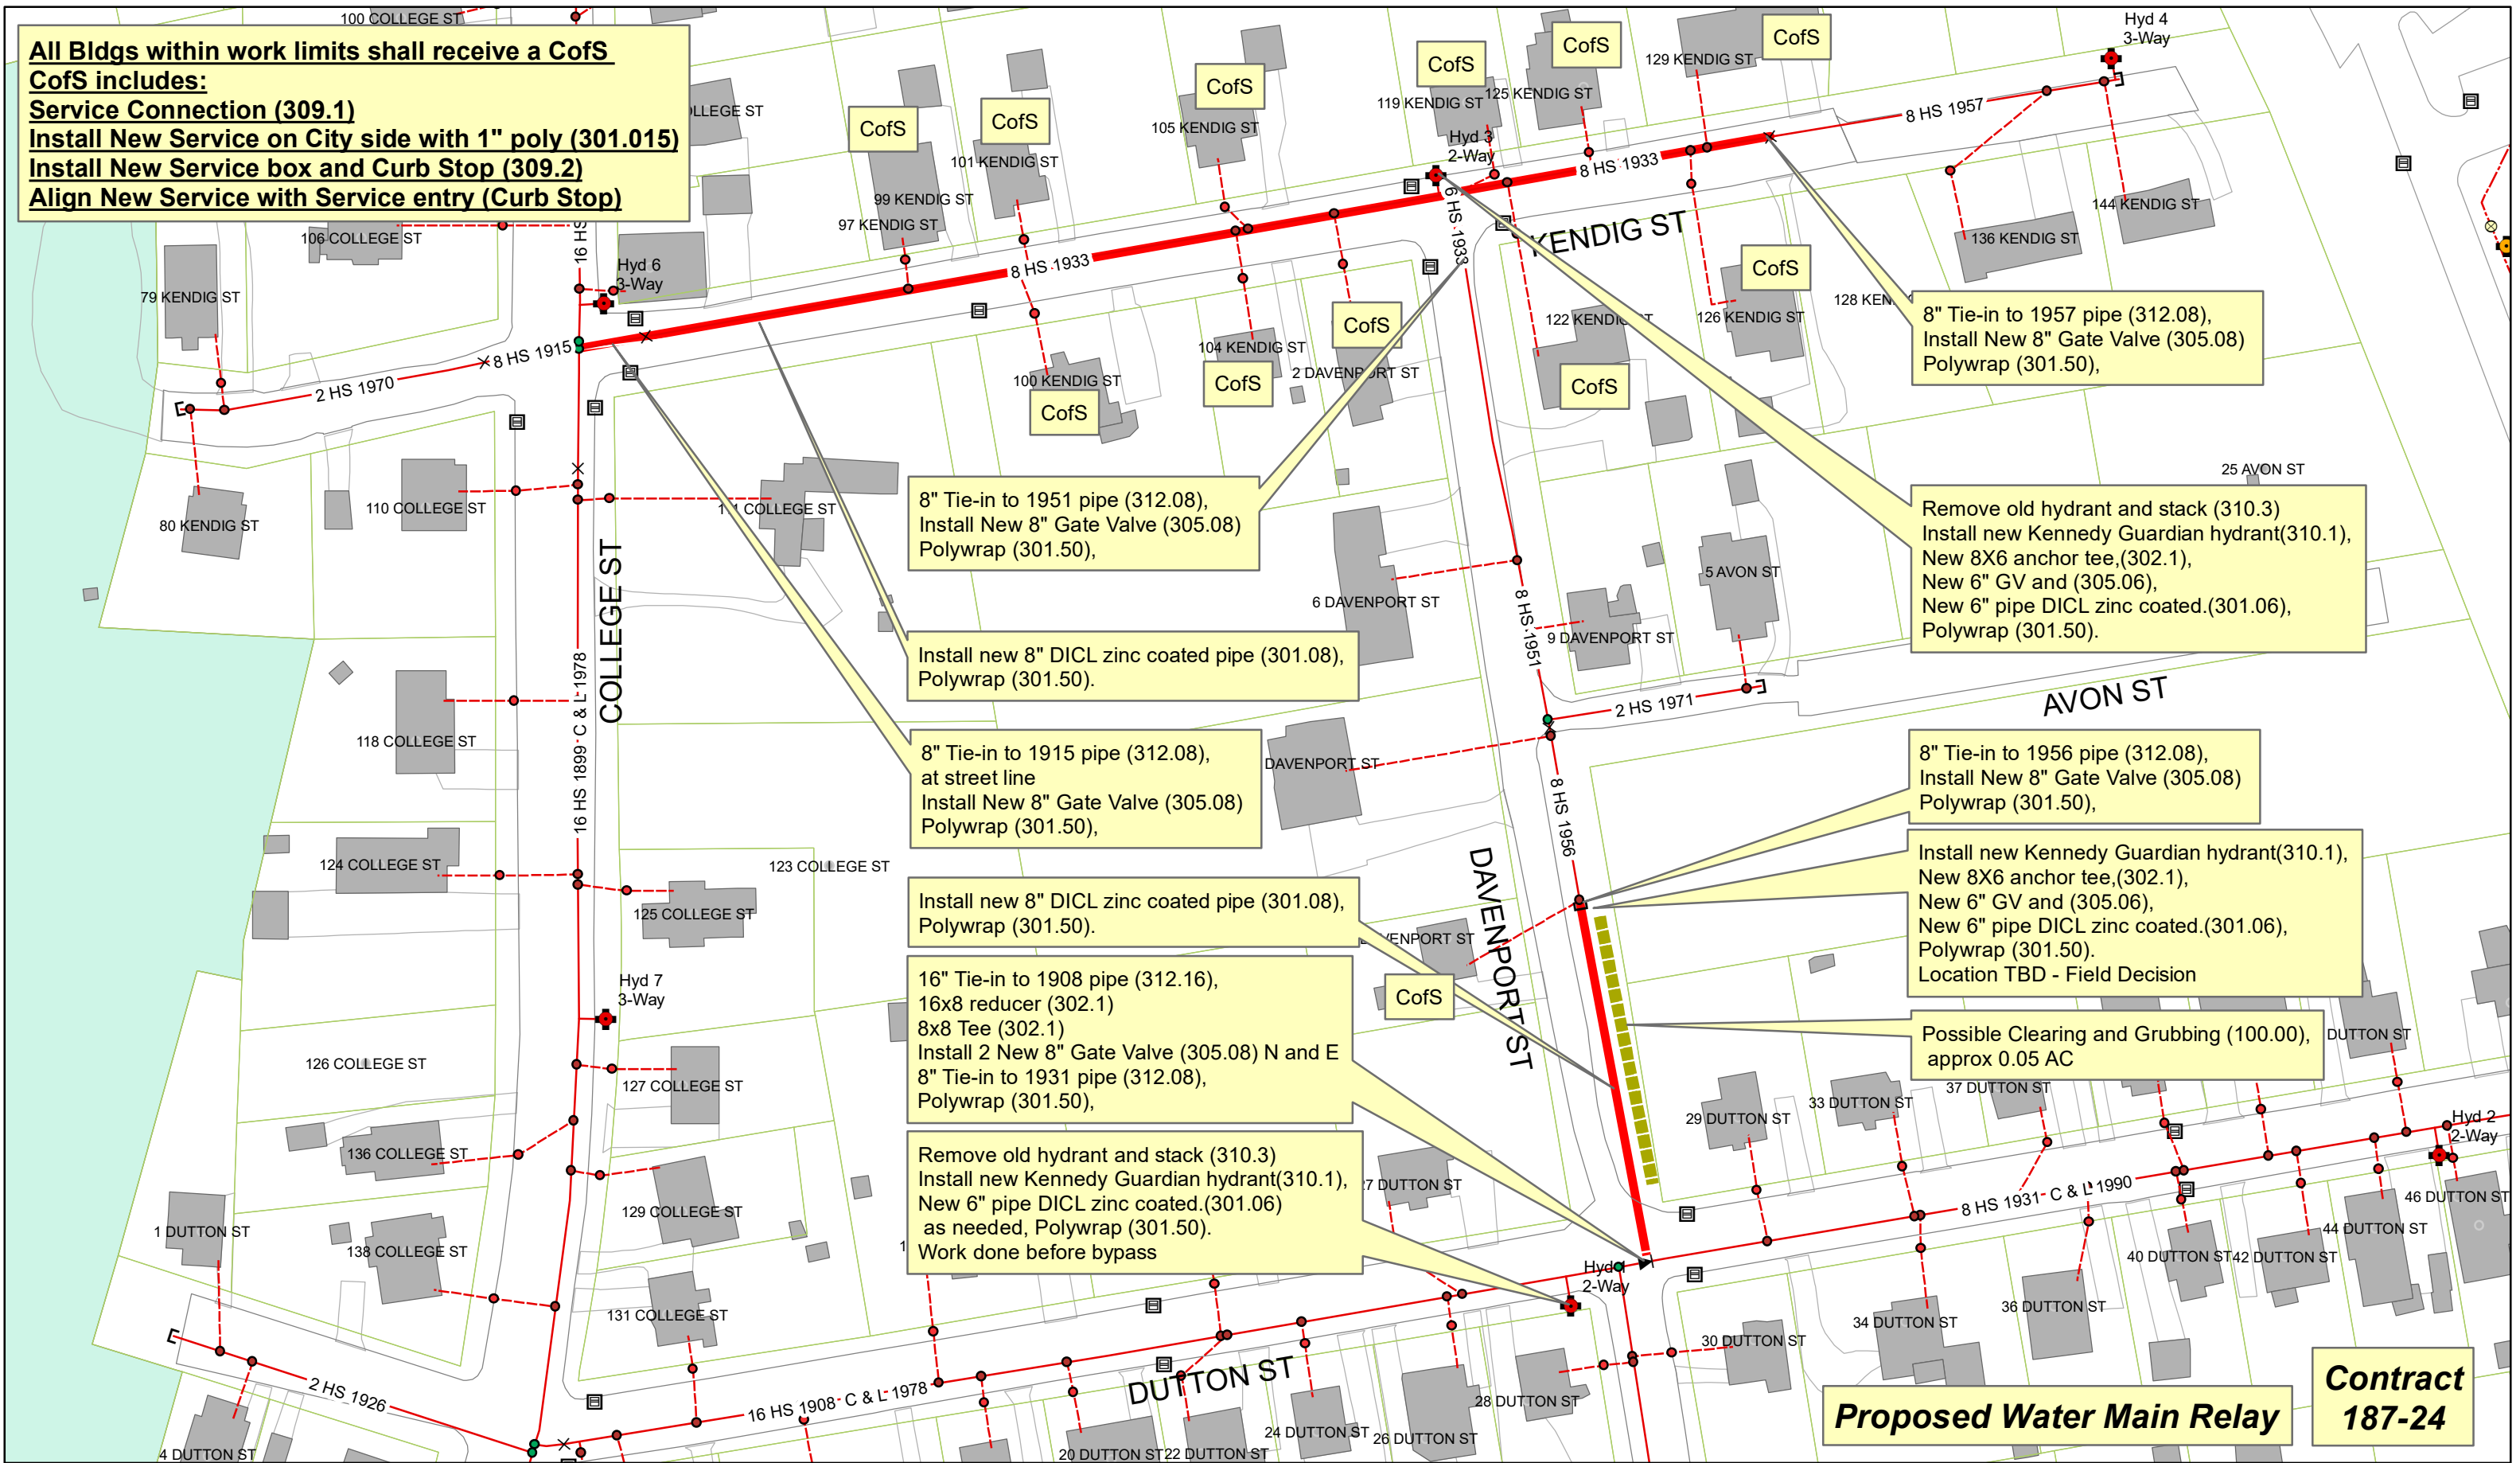


City Of Worcester
Department of Public Works & Parks
Water Operations



KENDIG STREET - Relay 665 Ft of 8" 1933 pipe
DAVENPORT STREET - Install 210 ft of new 8" pipe
and Interconnection to Dutton Street



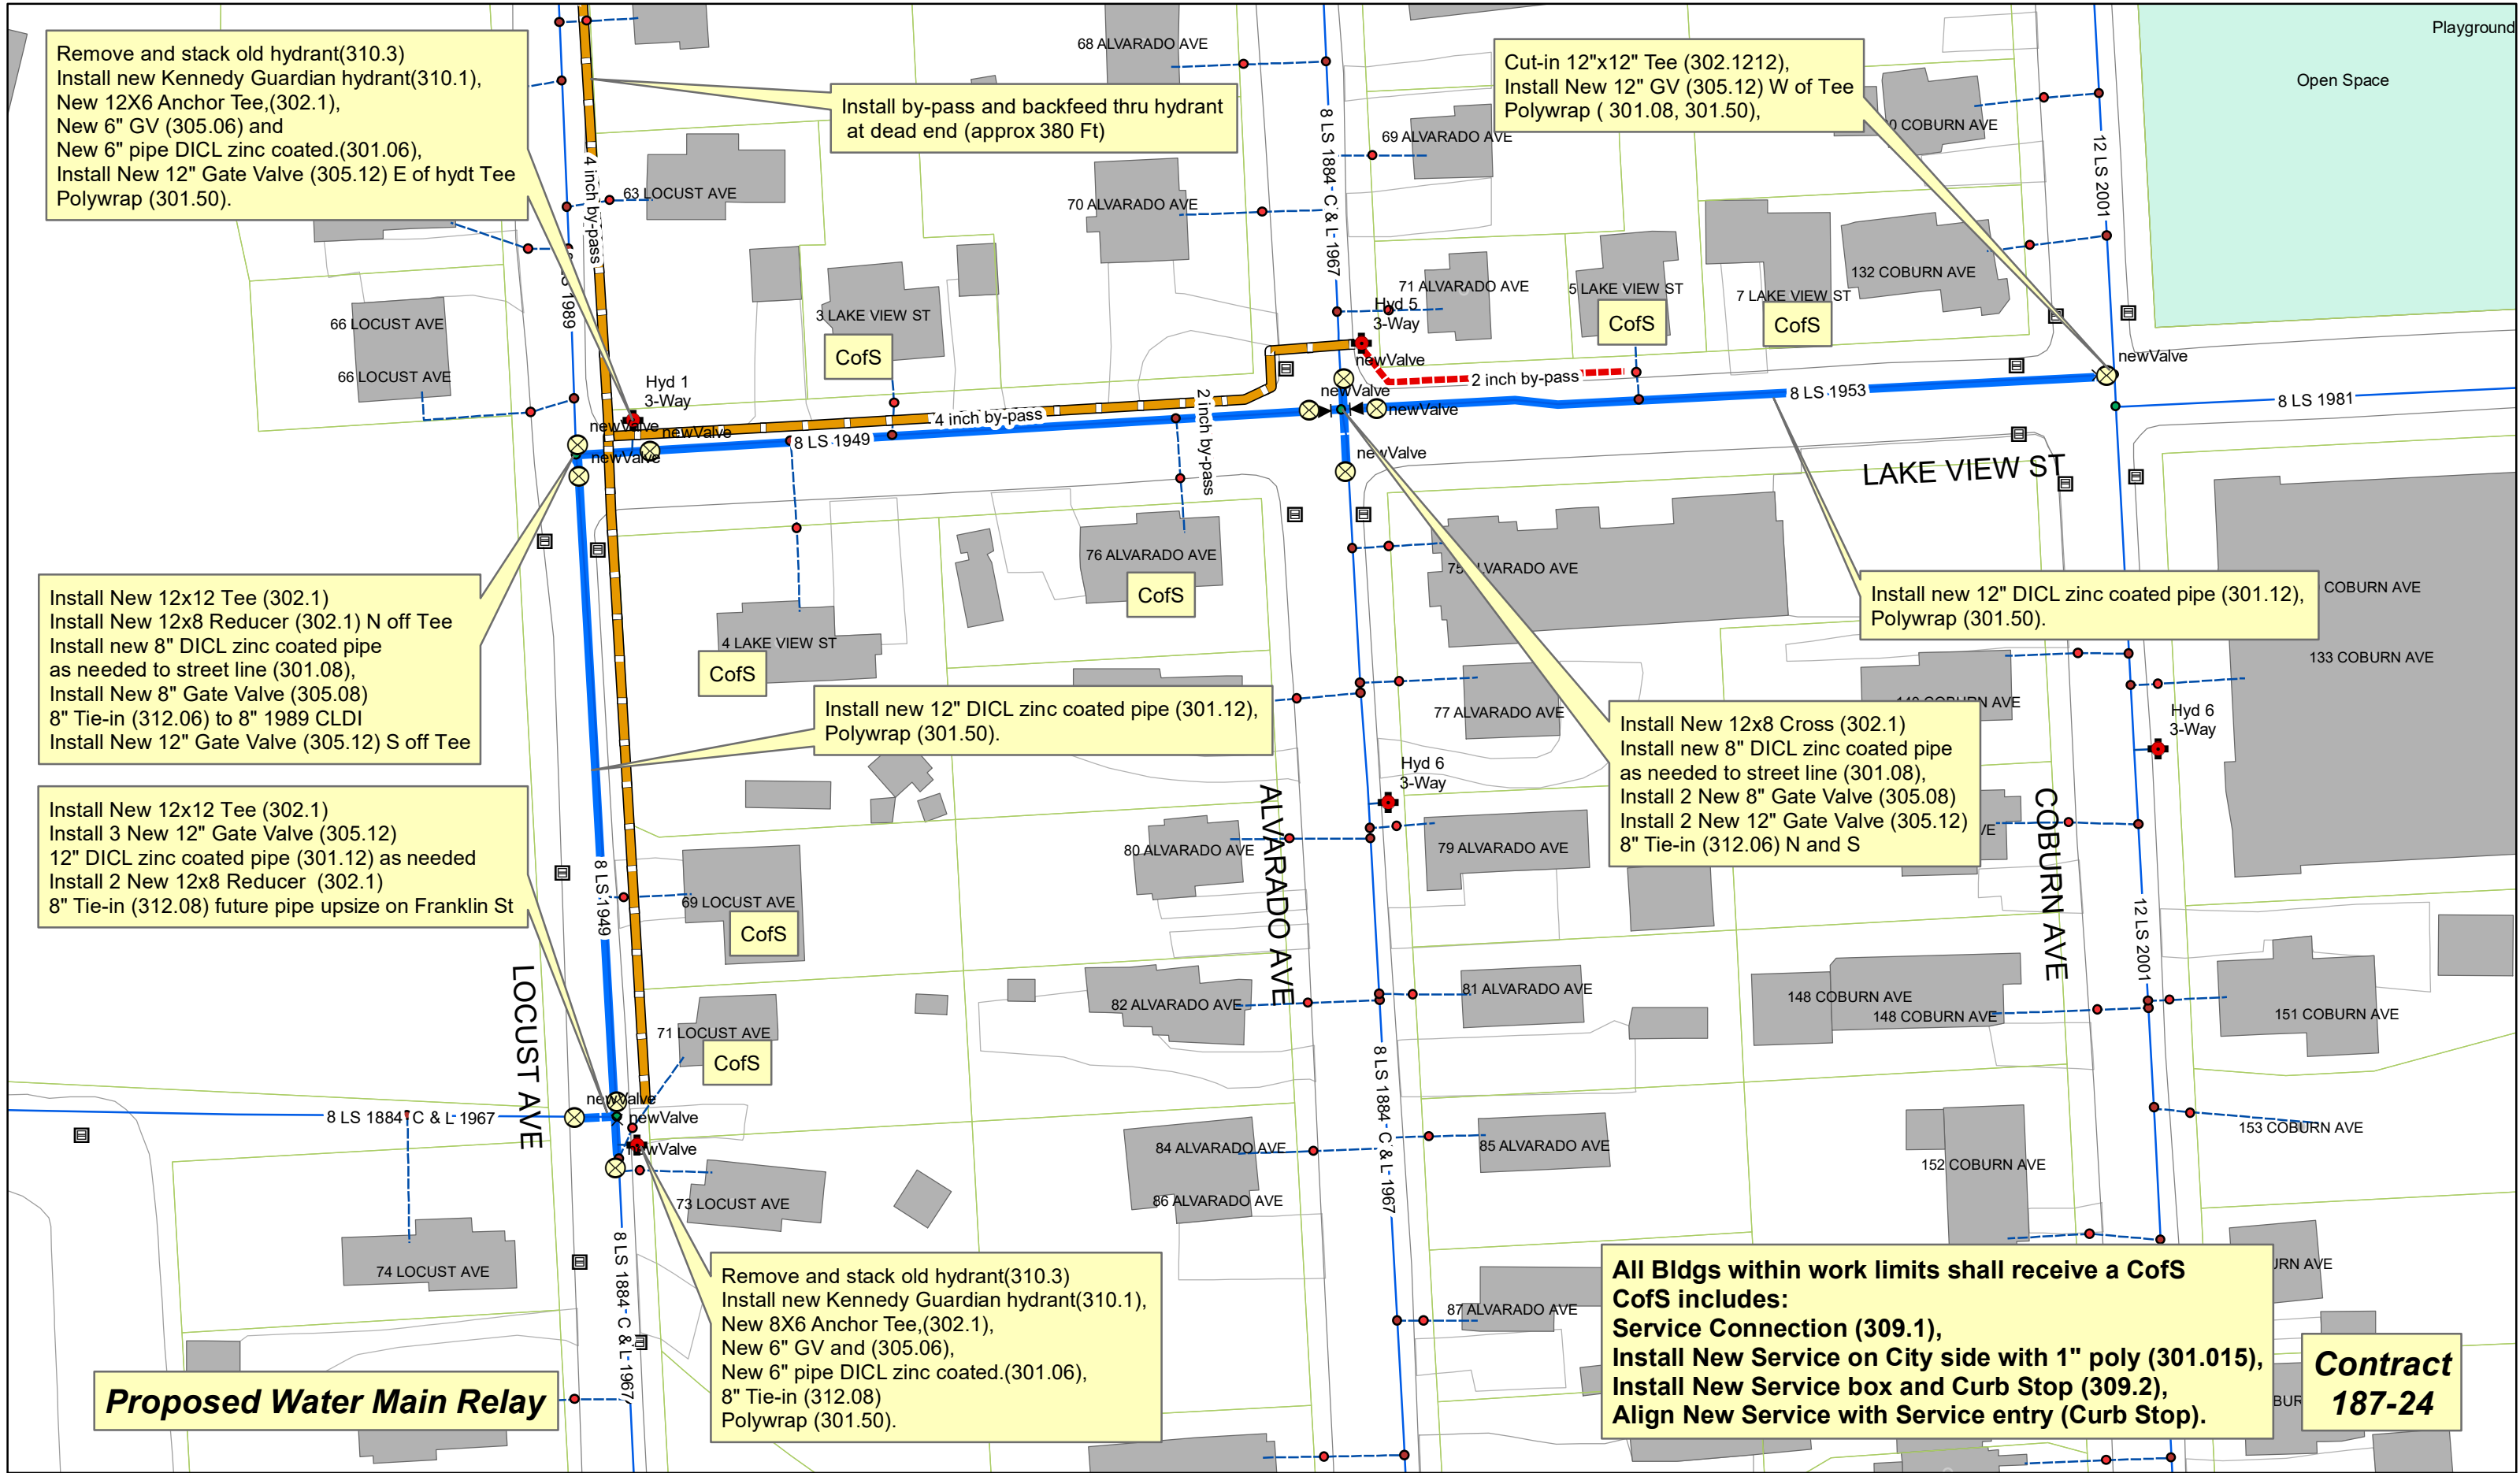

Remove and stack old hydrant(310.3)
Install new Kennedy Guardian hydrant(310.1),
New 12X6 Anchor Tee,(302.1),
New 6" GV (305.06) and
New 6" pipe DCLD zinc coated.(301.06),
Install New 12" Gate Valve (305.12) E of hydt Tee
Polywrap (301.50).

Install by-pass and backfeed thru hydrant
at dead end (approx 380 Ft)

Cut-in 12"x12" Tee (302.1212),
Install New 12" GV (305.12) W of Tee
Polywrap (301.08, 301.50),

Install New 12x12 Tee (302.1)
Install New 12x8 Reducer (302.1) N off Tee
Install new 8" DCLD zinc coated pipe
as needed to street line (301.08),
Install New 8" Gate Valve (305.08)
8" Tie-in (312.06) to 8" 1989 CLDI
Install New 12" Gate Valve (305.12) S off Tee

Install New 12x12 Tee (302.1)
Install 3 New 12" Gate Valve (305.12)
12" DCLD zinc coated pipe (301.12) as needed
Install 2 New 12x8 Reducer (302.1)
8" Tie-in (312.08) future pipe upsize on Franklin St

Install new 12" DCLD zinc coated pipe (301.12),
Polywrap (301.50).

Install new 12" DCLD zinc coated pipe (301.12),
Polywrap (301.50).

Install New 12x8 Cross (302.1)
Install new 8" DCLD zinc coated pipe
as needed to street line (301.08),
Install 2 New 8" Gate Valve (305.08)
Install 2 New 12" Gate Valve (305.12)
8" Tie-in (312.06) N and S


Remove and stack old hydrant(310.3)
Install new Kennedy Guardian hydrant(310.1),
New 8X6 Anchor Tee,(302.1),
New 6" GV and (305.06),
New 6" pipe DCLD zinc coated.(301.06),
8" Tie-in (312.08)
Polywrap (301.50).

All Bldgs within work limits shall receive a CofS
CofS includes:
Service Connection (309.1),
Install New Service on City side with 1" poly (301.015),
Install New Service box and Curb Stop (309.2),
Align New Service with Service entry (Curb Stop).

**Contract
187-24**




**City Of Worcester
Department of Public Works & Parks
Water Operations**



**LAKE VIEW ST Relay 900' of old 8" pipe
with new 12" CLDI zinc coated pipe**



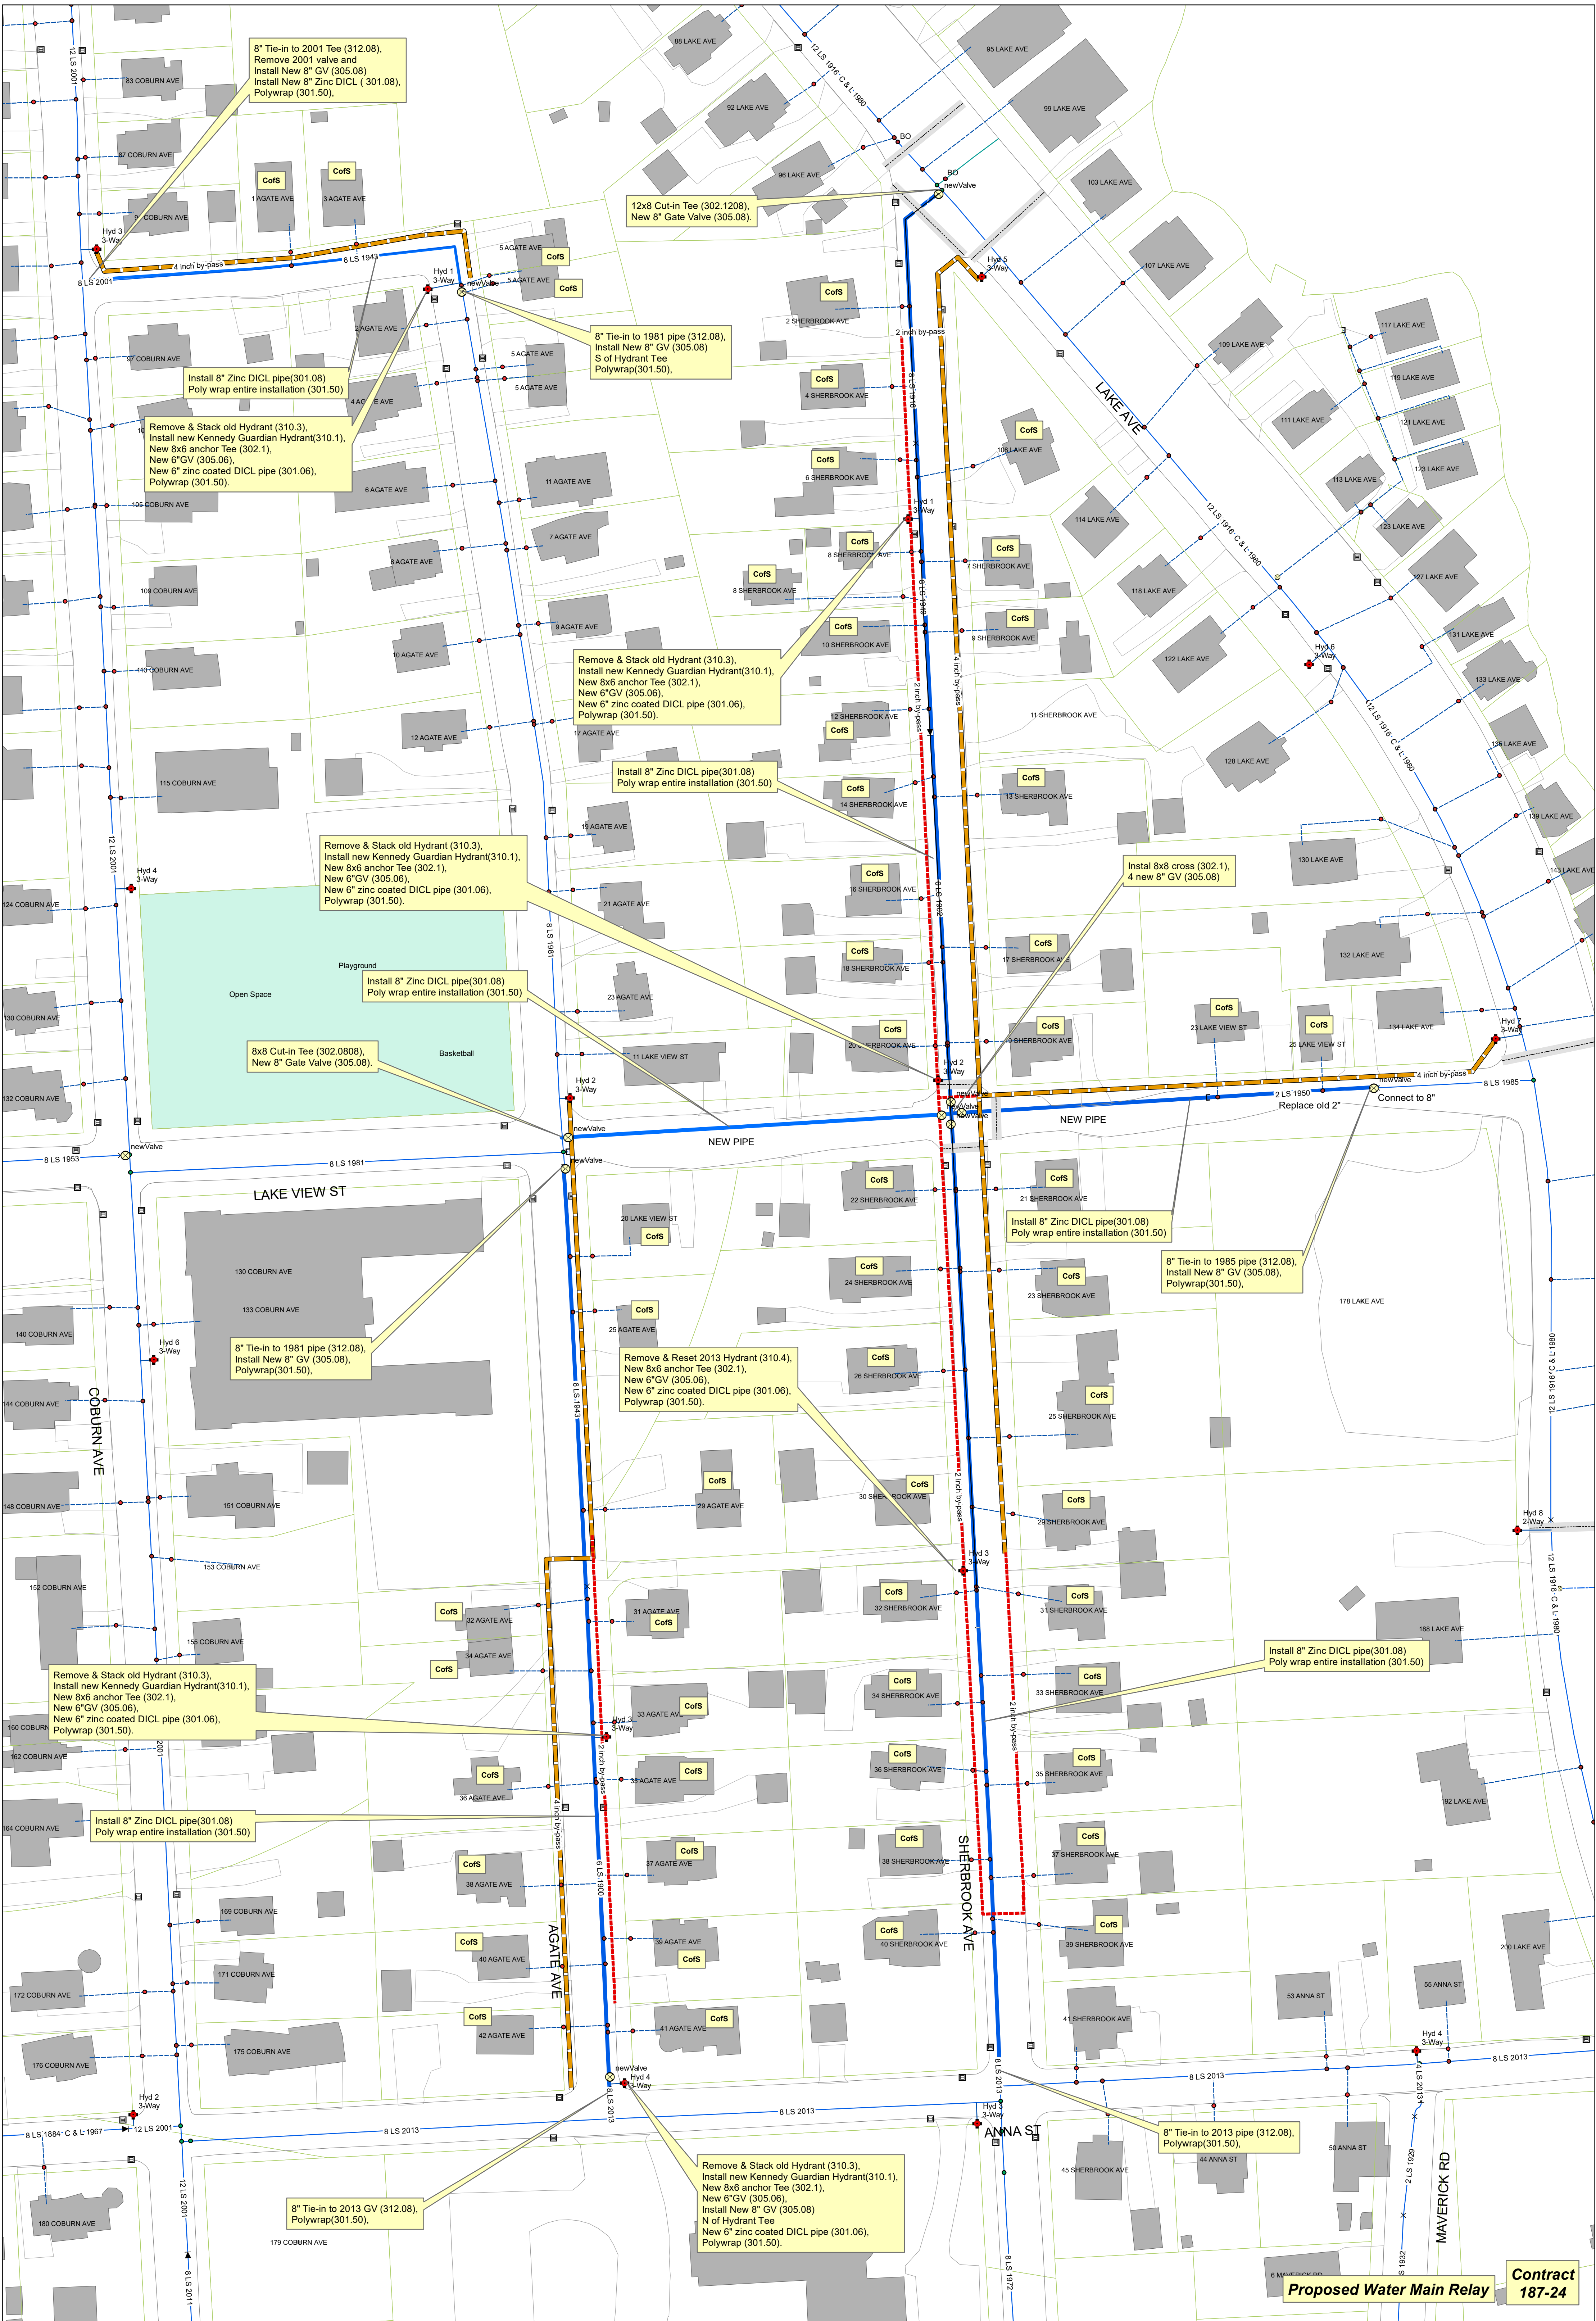

SHERBROOK AVE (Lake Ave S to Anna St)
Relay 985' of 6" 1902 & 420' 8" 1916-1949
LAKE VIEW ST (EOP near Lake Ave W to Agate Ave)
590' of new 8" replaces old 2" and eliminates dead end)
AGATE AVE (Anna St to Lake View St and Coburn Ave to #5)
965' of new 8" replaces old 6" 1943-1950 pipe.

